RESIDENTIAL ENERGY CONSERVATION CODE DOCUMENTATION CHECKLIST

Florida Department of Business and Professional Regulation Simulated Performance Alternative (Performance) Method

Applications for compliance with the 2020 Florida Building Code, Energy Conservation via the Residential Simulated Performance Alternative shall include:

	This checklist					
	Form R405-2020 report					
	Input summary checklist that can be used for field verification (usually four pages/may be greater)					
	Energy Performance Level (EPL) Display Card (one page)					
	HVAC system sizing and selection based on ACCA Manual S or per exceptions provided in Section R403.7					
	Mandatory Requirements (five pages)					
Red	quired prior to CO:					
	Air Barrier and Insulation Inspection Component Criteria checklist (Table R402.4.1.1 - one page)					
	A completed 2020 Envelope Leakage Test Report (usually one page); exception in R402.4 allows dwelling units of R-2 Occupancies and multiple attached single family dwellings to comply with Section C402.5					
	If Form R405 duct leakage type indicates anything other than "default leakage", then a completed 2020 Duct Leakage Test Report - Performance Method (usually one page)					

FLORIDA ENERGY EFFICIENCY CODE FOR BUILDING CONSTRUCTION

Florida Department of Business and Professional Regulation - Residential Performance Method

Project Name: 19TH ST SW Street: 19TH ST SW City, State, Zip: NAPLES , FL, 34117 Owner: PEREZ REINIER & MASSIEL SANABRIA Design Location: FL, NAPLES_MUNICIPAL	Builder Name: Permit Office: COLLIER COUNTY Permit Number: Jurisdiction: 211200 County: Collier(Florida Climate Zone 1)
1. New construction or existing 2. Single family or multiple family 3. Number of units, if multiple family 4. Number of Bedrooms 5. Is this a worst case? 6. Conditioned floor area above grade (ft²) Conditioned floor area below grade (ft²) Conditioned floor area below grade (ft²) 7. Windows(209.7 sqft.) Description a. U-Factor: Sgl, U=0.55 SHGC: SHGC=0.25 b. U-Factor: N/A SHGC: C. U-Factor: N/A SHGC: Area Weighted Average Overhang Depth: Area Weighted Average SHGC: 8. Skylights U-Factor:(AVG) SHGC(AVG): N/A 9. Floor Types Insulation a. Slab-On-Grade Edge Insulation B. N/A R= ft² R= ft² ft² ft²	10. Wall Types(1893.1 sqft.) a. Concrete Block - Int Insul, Exterior R=4.1 1712.70 ft² b. Frame - Wood, Adjacent R=13.0 180.44 ft² c. N/A R= ft² d. N/A R= ft² 11. Ceiling Types(1615.0 sqft.) a. Flat ceiling under att (Vented) R=30.0 1615.00 ft² b. N/A R= ft² c. N/A R= ft² 12. Ducts, location & insulation level a. Sup: Attic, Ret: Attic, AH: Attic b. c. 13. Cooling Systems kBtu/hr Efficiency a. Central Unit 30.0 SEER:14.00 14. Heating Systems a. Electric Heat Pump 23.5 HSPF:12.00 15. Hot Water Systems a. Electric Cap: 40 gallons EF: 2.500 b. Conservation features None 16. Credits
Glass/Floor Area: 0.130 Total Proposed Modifie Total Baselin	ed Loads: 58.37
I hereby certify that the plans and specifications covered by this calculation are in compliance with the Florida Energy Code. PREPARED BY: RICARDO MENDEZ DATE: 4-1-22 I hereby certify that this building, as designed, is in compliance with the Florida Energy Code. OWNER/AGENT: OSJR DATE: 06/20/2022 - Compliance requires certification by the air handler unit m	Review of the plans and specifications covered by this calculation indicates compliance with the Florida Energy Code. Before construction is completed this building will be inspected for compliance with Section 553.908 Florida Statutes. BUILDING OFFICIAL: DATE:

- certified factory-sealed in accordance with R403.3.2.1.
- Default duct leakage does not require a Duct Leakage Test Report.
- Compliance requires an Air Barrier and Insulation Inspection Checklist in accordance with R402.4.1.1 and this project requires a PERFORMANCE envelope leakage test report with envelope leakage no greater than 7.00 ACH50 (R402.4.1.2).

INPUT SUMMARY CHECKLIST REPORT

					PRO	JECT						
Owner Build Perm Jurise Fami New/ Year	ingType:	19TH ST SW User PEREZ REINIER COLLIER COUNT 211200 Detached New (From Plans) 2022 NEW HOME	& MASSIEL SANAB Y	Total Sto Worst Ca Rotate A Cross Ve	nedArea: ories: ase: ngle: entilation: ouse Fan:	3 1615 1 No 0 No No Suburbar Suburbar	Lot # Bloc PlatE Stree Coul City,	k/SubDivisi Book: et:	 19TH ST S Collier			
					CLIN	IATE						
Des Loca	ign ation		Tmy Site		Des 97.5%	ign Temp 2.5%	Int Desig Winter		Heating Degree Days	Desigr Moisture		lytemp nge
FL	, NAPLES_M	IUNICIPAL	FL_NAPLES_MUNI	CIPAL	46	90	70	75	288.5	58	Mediu	ım
					BLO	CKS						
V Nun	nber	Name	Area	Vo	olume							
1		Block1	1615	15	181 cu ft							
					SPA	CES						
V Nun	nber	Name	Area	Volume	Kitchen	Occupan	ts Bedr	ooms	Finished	Cool	led H	eated
1		Main	1615	15181	Yes	5	;	3	Yes	Υe	es	Yes
					FLO	ORS	(Total E	xposed Are	ea = 16	615 sq	.ft.)
V #	FloorTyp	e	Space	Exposed	Perim	PerimeterR-\	/alue Area	U-Facto	or Joist R-Value	e Tile '	Wood	Carpet
1	Slab-On-Gr	ade Edge Ins	Main	183	.8	0	1615	ft 0.71	0	1.00	0.00	0.00
					RO	OF						
\ #	Туре		Materials		Roof Area	Gable Ro Area Col		Solar Absor.	SA Emit Tested	t Emitt Tested	Deck Insul.	Pitch (deg)
1	Hip		Compositionshingle	s 1	806 ft²	0 ft ² Med	ium N	0.96	No 0.9	No	0	26.57
					ΑT	TIC						
/ #	Туре		Ventilation		Vent F	Ratio (1 in)	Area	RBS	IRCC	;		
1	Full attic		Vented			150	1615 ft²	N	N			
					CEIL	ING	(Total E	xposed Are	ea = 16	615 sq	.ft.)
V #	CeilingTy	/pe		Space	R-V	alue Ins. T	ype Are	ea U-F	actor Framin	g Frac.	Truss	з Туре
1	Flat ceiling	under attic(Vented)		Main	30	0.0 Blov	wn 1615	.0ft² 0.	053 0.	11	W	ood

INPUT SUMMARY CHECKLIST REPORT

								WA	LLS	3		(Tot	al Exp	osed .	Area	= 189)3 sq.	ft.)
\ #	Orı		jacent To	Wall Type		Space		Ca R-\	vity /alue	Width Ft In		Height Ft In	Area sq.ft	u U- . Factor	Sheath R-Valu		Solar . Absor.	Below Grade
	1 N 2 E 3 S 4 V 5 E	} V	Exterior Exterior Exterior Exterior Garage	Conc. Blk - In Conc. Blk - In Conc. Blk - In Conc. Blk - In Frame - Woo	nt Ins nt Ins nt Ins	N N N	lain lain lain lain lain	2	4.1 4.1 4.1 4.1 3.0	50.0 £ 41.0 £ 41.0 £ 19.0 £	4 ! 5 ! 4 !	9.0 4 9.0 4 9.0 4 9.0 4 9.0 4	385.8 470.0 385.8	3 0.149 6 0.149 3 0.149	0 0	0 0 0 0 0.23	0.75 0.75 0.75 0.75 0.75	0 % 0 % 0 % 0 %
	DOORS (Total Exposed Area = 0 sq.ft.)																	
\ #	Ori	nt	Adjacent	To DoorType		Space			Stori	ms	l	J-Value		Vidth Ft In		eight : In	Are	ea
	1 N	1		Wood		Mair	Ì		No	ne		0.20	0.0	0 0	0.00	0	0.0	lft²
	WINDOWS (Total Exposed Area = 210 sq.ft.)																	
\ #	Ori	Wall nt ID	Frame	Panes	NFRC	U-Factor	SHGC	Imp	Storm	Total Area (ft²)	Same Units	Width (ft)	Height (ft)	Overh Depth (ft)		Interior	Shade	Screen
2 3 4 5 6 7	E W	1 1 2 2 2 4 4	Metal Metal Metal Metal Metal Metal Metal Metal Metal	Single (Clear)	Y Y Y Y Y Y	0.55 0.55 0.55 0.55 0.55 0.55 0.55	0.25 0.25 0.25 0.25 0.25 0.25 0.25 0.25	Y Y Y Y Y Y	N N N N N N	32.4 9.9 48.0 12.0 14.1 32.4 48.0 12.9	2 1 1 1 2 2 1	3.08 3.08 6.00 6.00 2.21 3.08 6.00 3.08	5.25 3.20 8.00 2.00 3.20 5.25 8.00 4.20	1.3 1.3 1.3 1.3 1.3 1.3 1.3	1.3 1.3 1.3 1.3 1.3 1.3 1.3	No No No No No No No	ne ne ne ne ne ne	None None None None None None
							INF	ILT	RAT	ION								
V #	Sc	оре	Me	ethod	SI	_A (CFM50	E	LA	EqL	Ą	ACH	ACH5	i0 Spac	e(s)	Infiltra	tion Test	Volume
	1 V	Vholeho	ouse Prop	posed ACH(50)	0.00	0042	1771	97	7.17	182.4	2	0.1348	7.0	Al	II	15181	cu ft	
							(GAF	RAG	E								
V #			FloorArea		Roof Area	a	Ex	posed	Wall Pe	erimeter		Av	g. Wall He	eight	Exp	osed Wa	all Insulat	tion
	1		330 ft ²		330 ft²				53 ft				9 ft			4	ļ	
								MA	ASS									
V #	N	/lass Ty	ре		Ar	ea		Tł	nicknes	s	Fur	nitureFr	action	5	Space			
	1 [Default(8	3 lbs/sq.ft.)		0	ft²			0 ft			0.30			Main			
							HEAT	ΓINC	SY	STE	VI							
V #	8	System	Гуре		Subtype/\$	Speed	AHR	l #	Effici	iency	Capa kBtu			hermalHe Power	eatPump Volt C		Oucts	Block
	1 E	Electric I	Heat Pump		Split/Sir	ngle			HSPF:	: 12.00	23.	5		0.00	0.00	0.00 s	ys#1	1

INPUT SUMMARY CHECKLIST REPORT

					CC	OLII	NG SYS	STEM						
V #	SystemType		Sub	otype/Spee	d	AHRI #	Effic	ciency	Capacity kBtu/hr		r Flow cfm	SHR	Duct	Block
1	Central Unit			Split/Singl	е		SEE	R:14.0 3	0.0	!	900	0.75	sys#1	1
					НОТ	WA	TER S	YSTEM						
V #	SystemType	Subtype		Location		EF(UE	F) Cap	Use	SetPnt	Fixture	Flow	Pipe Ins	. Pipe	elength
1	Electric	Heat Pum	р	Garage		2.50 (2.	57) 40.00 (gal 70 gal	120 deg	Stan	dard	=>R-3		25
	Recirculation System		c Control Type		Loop length	Brand lengt			R Faciliti Connec			DWHR Eff	Othe	r Credits
1	No				NA	NA	NA	No	NA	N	A	NA	Non	е
	DUCTS													
√Du / #	ctSu Location	pply R-Value A	rea Loc	Ret ation	urn R-Value		Leakage	еТуре	Air Handler	CFM 25 TOT	CFM 25 OUT	5 QN	RLF H	HVAC # eat Cool
1	Attic	6.0 323	ft ² Attic		6.0	81 ft ²	DefaultLe	eakage	Attic	(Default) (Default)			1 1
					TI	EMPI	ERATU	RES						
Coo Hea	gramableThermo bling []Jan ating [X]Jan nting []Jan	ostat: Y [] Feb [X] Feb [] Feb	[] Mar [X] Mar [X] Mar	[] Apr [] Apr [X] Apr	[] N [] N [] N	1ay	ans: N [X] Jun [] Jun [] Jun	[X] Jul [] Jul [] Jul	[X] Aug [] Aug [] Aug	[X] Sep [] Sep [] Sep	[]0 []0 [X]C	ct [X] Nov K] Nov K] Nov	[] Dec [X] Dec [] Dec
	hermostat Sched	lule: HERS 2	006 Referen	ce 2	3	4	5	Hoi 6	urs 7	8	9	10	11	12
· .	Cooling (WD)	AM PM	78 80	78 80	78 78	78 78	78 78	78 78	78 78	78 78	80 78	80 78	80 78	80 78
	Cooling (WEH)	AM PM	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78
F	leating (WD)	AM PM	66 68	66 68	66 68	66 68	66 68	68 68	68 68	68 68	68 68	68 68	68 66	68 66
	leating (WEH)	AM PM	66 68	66 68	66 68	66 68	66 68	68 68	68 68	68 68	68 68	68 68	68 66	68 66

ENERGY PERFORMANCE LEVEL (EPL) DISPLAY CARD ESTIMATED ENERGY PERFORMANCE INDEX* = 96

The lower the EnergyPerformance Index, the more efficient the home.

19TH ST SW, NAPLES ,FL, 34117

1.	New construction or ex	isting	New (From Plan	s) 10.	Wall Types(1893.1 sqft.)	Insulatio		Area
2.	Single family or multipl	e family	Detach	Ju	Concrete Block - Int Insul, Exterior		1712.	70 ft ²
3.	Number of units, if mul	tiple family		1	Frame - Wood, Adjacent N/A	R=13.0 R=	180.	44 ft ²
4.	Number of Bedrooms				N/A	R=		ft ²
5.	Is this a worst case?		1	••	Ceiling Types(1615.0 sqft.)	Insulatio		Area
6.	Conditioned floor area Conditioned floor area	•	•	15 0 b.	Flat ceiling under att (Vented) N/A N/A	R=30.0 R= R=		00 ft ² ft ²
а	Windows** . U-Factor: SHGC: . U-Factor:	Description Sgl, U=0.55 SHGC=0.25 N/A	Ard 209.68	ea 12.	Ducts, location & insulation level Sup: Attic, Ret: Attic, AH: Attic		R 6	ft ²
С	SHGC: . U-Factor: SHGC:	N/A		13.	Cooling Systems Central Unit	kBtu/hr 30.0	Effic SEER:	iency 14.00
A 8.	rea Weighted Average (rea Weighted Average Skylights U-Factor:(AVG)		n: 1.333 0.29 Ard N/A	50 14. _{ea_} a.	Heating Systems Electric Heat Pump	kBtu/hr 23.5	Effic HSPF:	iency 12.00
a b	SHGC(AVG): Floor Types . Slab-On-Grade Edge . N/A . N/A			ea 0 ft ² a. ft ²	Hot Water Systems Electric Conservation features	Ca _l		2.500
					Credits			None Pstat

I certify that this home has complied with the Florida Energy Efficiency Code for Building Construction through the above energy saving features which will be installed (or exceeded) in this home before final inspection. Otherwise, a new EPL Display Card will be completed based on installed Code compliant features.

Builder Signature:	Date:
Address of New Home: 19TH ST SW	City/FL Zin: NAPLES EL 3/117

*Note: This is not a Building Energy Rating. If your Index is below 70, your home may qualify for energy efficient mortgage (EEM) incentives if you obtain a Florida Energy Rating. For information about the Florida Building Code, Energy Conservation, contact the Florida Building Commission's support staff.

**Label required by Section R303.1.3 of the Florida Building Code, Energy Conservation, if not DEFAULT.



Residential System Sizing Calculation

Summary

PEREZ REINIER & MASSIEL SANABRIA 19TH ST SW NAPLES , FL 34117 Project Title: 19TH ST SW

NEW HOME


4/1/2022

Location for weather data: Naples, FL - Defaults: Latitude(26.15) Altitude(3 ft.) Temp Range(M)					
Humidity data: Interior RH (50%) Outdoor wet bulb (78F) Humidity difference(58gr.)					
Winter design temperature(TMY3	99%) 43	F	Summer design temperature(TMY	′ 3 99%) 91	F
Winter setpoint	70	F	Summer setpoint	75	F
Winter temperature difference	27	F	Summer temperature difference	16	F
Total heating load calculation	21458	Btuh	Total cooling load calculation	30769	Btuh
Submitted heating capacity	% of calc	Btuh	Submitted cooling capacity	% of calc	Btuh
Total (Electric Heat Pump)	109.3	23463	Sensible (SHR = 0.75)	91.1	22500
Heat Pump + Auxiliary(0.0kW)	109.3	23463	Latent	123.4	7500
			Total (Flectric Heat Pump)	97.5	30000

WINTER CALCULATIONS

Winter Heating Load (for 1615 sqft)


Load component			Load	
Window total	210	sqft	3114	Btuh
Wall total	1683	sqft	6488	Btuh
Door total	0	sqft	0	Btuh
Ceiling total	1615	sqft	1389	Btuh
Floor total	1615	sqft	5856	Btuh
Infiltration	55	cfm	1620	Btuh
Duct loss			2991	Btuh
Subtotal			21458	Btuh
Ventilation	Ex:0 cfm; Sup:0	cfm	0	Btuh
TOTAL HEAT LO	21458	Btuh		



SUMMER CALCULATIONS

Summer Cooling Load (for 1615 sqft)

Load component			Load	
Window total	210	sqft	6202	Btuh
Wall total	1683	sqft	3912	Btuh
Door total	0	sqft	0	Btuh
Ceiling total	1615	sqft	2109	Btuh
Floor total			0	Btuh
Infiltration	41	cfm	720	Btuh
Internal gain			7950	Btuh
Duct gain			3796	Btuh
Sens.Ventilation	Ex:0 cfm; Sup:0	cfm cfm	0	Btuh
Blower Load			0	Btuh
Total sensible gair	า		24689	Btuh
Latent gain(ducts)			1066	Btuh
Latent gain(infiltration	on)		1613	Btuh
Latent gain(ventilati	0	Btuh		
Latent gain(internal/	3400	Btuh		
Total latent gain			6080	Btuh
TOTAL HEAT GAIN	١		30769	Btuh

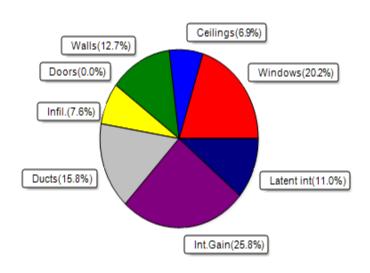



EnergyGauge® System Sizing
PREPARED BY:RICARDO MENDEZ
DATE: 04/01/2022

Florida Building Code, Energy Conservation, 7th Edition (2020) Mandatory Requirements for Residential Performance, Prescriptive and ERI Methods

ADDRESS:	19TH ST SW	Permit Number:	
	NAPLES . FL 34117		

MANDATORY REQUIREMENTS - See individual code sections for full details.

SECTION R401 GENERAL
R401.3 Energy Performance Level (EPL) display card - (Mandatory). The building official shall require that an energy performance level (EPL) display card be completed and certified by the builder to be accurate and correct before final approval of the building for occupancy. Florida law (Section 553.9085, Florida Statutes) requires the EPL display card to be included as an addendum to each sales contract for both presold and nonpresold residential buildings. The EPL display card contains information indicating the energy performance level and efficiencies of components installed in a dwelling unit. The building official shall verify that the EPL display card completed and signed by the builder accurately reflects the plans and specifications submitted to demonstrate code compliance for the building. A copy of the EPL display card can be found in Appendix RD.
SECTION R402 BUILDING THERMAL ENVELOPE
R402.4 Air leakage (Mandatory). The building thermal envelope shall be constructed to limit air leakage in accordance with the requirements of Sections R402.4.1 through R402.4.5.
Exception: Dwelling units of R-2 Occupancies and multiple attached single family dwellings shall be permitted to comply with Section C402.5.
R402.4.1 Building thermal envelope. The building thermal envelope shall comply with Sections R402.4.1.1 and R402.4.1.2. The sealing methods between dissimilar materials shall allow for differential expansion and contraction.
R402.4.1.1 Installation. The components of the building thermal envelope as listed in Table R402.4.1.1 shall be installed in accordance with the manufacturer's instructions and the criteria listed in Table R402.4.1.1, as applicable to the method of construction. Where required by the code official, an approved third party shall inspect all components and verify compliance.
R402.4.1.2 Testing. The building or dwelling unit shall be tested and verified as having an air leakage rate not exceeding seven air changes per hour in Climate Zones 1 and 2, and three air changes per hour in Climate Zones 3 through 8. Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the code official. Testing shall be performed at any time after creation of all penetrations of the building thermal envelope.
Exception: Testing is not required for additions, alterations, renovations, or repairs, of the building thermal envelope of existing buildings in which the new construction is less than 85 percent of the building thermal envelope.
During testing: 1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration control measures. 2. Dampers including exhaust, intake, makeup air, backdraft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures. 3. Interior doors, if installed at the time of the test, shall be open. 4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed. 5. Heating and cooling systems, if installed at the time of the test, shall be turned off. 6. Supply and return registers, if installed at the time of the test, shall be fully open.
R402.4.2 Fireplaces. New wood-burning fireplaces shall have tight-fitting flue dampers or doors, and outdoor combustion air. Where using tight-fitting doors on factory-built fireplaces listed and labeled in accordance with UL 127, the doors shall be tested and listed for the fireplace. Where using tight-fitting doors on masonry fireplaces, the doors shall be listed and labeled in accordance with UL 907.
R402.4.3 Fenestration air leakage. Windows, skylights and sliding glass doors shall have an air infiltration rate of no more than 0.3 cfm per square foot (1.5 L/s/m2), and swinging doors no more than 0.5 cfm per square foot (2.6 L/s/m2), when tested according to NFRC 400 or AAMA/WDMA/CSA 101/I.S.2/A440 by an accredited, independent laboratory and listed and labeled by the manufacturer.
Exception: Site-built windows, skylights and doors.

Exceptions:

1. Direct vent appliances with both intake and exhaust pipes installed continuous to the outside.

R402.4.4 Rooms containing fuel - burning appliances. In Climate Zones 3 through 8, where open combustion air ducts provide combustion air to open combustion fuel burning appliances, the appliances and combustion air opening shall be located outside the building thermal envelope or enclosed in a room, isolated from inside the thermal envelope. Such rooms shall be sealed and insulated in accordance with the envelope requirements of Table R402.1.2, where the walls, floors and ceilings shall meet not less than the basement wall R-value requirement. The door into the room shall be fully gasketed and any water lines and ducts in the room insulated in accordance with Section R403. The combustion air duct shall be insulated where it passes through conditioned space to a minimum of R-8.

2. Fireplaces and stoves complying with Section R402.4.2 and Section R1006 of the Florida Building Code, Residential.

MANDATORY REQUIREMENTS (Continued)

	not more than 2.0 cfm (0.944 L/s) when tested in accordance with ASTM E283 at a 1.57 psf (75 Pa) pressure differential. All recessed luminaires shall be sealed with a gasket or caulk between the housing and the interior wall or ceiling covering.
	SECTION R403 SYSTEMS
	R403.1 Controls R403.1.1 Thermostat provision (Mandatory). At least one thermostat shall be provided for each separate heating and cooling system
	R403.1.3 Heat pump supplementary heat (Mandatory). Heat pumps having supplementary electric-resistance heat shall have controls that, except during defrost, prevent supplemental heat operation when the heat pump compressor can meet the heating load.
	R403.3.2 Sealing (Mandatory). All ducts, air handlers, filter boxes and building cavities that form the primary air containment passageways for air distribution systems shall be considered ducts or plenum chambers, shall be constructed and sealed in accordance with Section C403.2.9.2 of the Commercial Provisions of this code and shall be shown to meet duct tightness criteria below.
	Duct tightness shall be verified by testing in accordance with ANSI/RESNET/ICC 380 by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i), Florida Statutes, to be "substantially leak free" in accordance with Section R403.3.3.
	R403.3.2.1 Sealed air handler. Air handlers shall have a manufacturer's designation for an air leakage of no more than 2 percent of the design airflow rate when tested in accordance with ASHRAE 193.
	R403.3.3 Duct testing (Mandatory). Ducts shall be pressure tested to determine air leakage by one of the following methods: 1. Rough-in test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the system, including the manufacturer's air handler enclosure if installed at the time of the test. All registers shall be taped or otherwise sealed during the test.
	2 Postconstruction test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the entire system, including the manufacturer's air handler enclosure. Registers shall be taped or otherwise sealed during the test. Exceptions;
	 A duct air leakage test shall not be required where the ducts and air handlers are located entirely within the building thermalenvelope.
	2. Duct testing is not mandatory for buildings complying by Section 405 of this code. Duct leakage testing is required for Section R405 compliance where credit is taken for leakage, and a duct air leakage Qn to the outside of less than 0.080 (where Qn = duct leakage to the outside in cfm per 100 square feet of conditioned floor area tested at 25 Pascals) is indicated in the compliance report for the proposed design.
П	A written report of the results of the test shall be signed by the party conducting the test and provided to the code official
	R403.3.5 Building cavities (Mandatory). Building framing cavities shall not be used as ducts or plenums
	R403.4 Mechanical system piping insulation (Mandatory). Mechanical system piping capable of carrying fluids above 105°F (41°C) or below 55°F (13°C) shall be insulated to a minimum of R-3.
	R403.4.1 Protection of piping insulation. Piping insulation exposed to weather shall be protected from damage, including that caused by sunlight, moisture, equipment maintenance and wind, and shall provide shielding from solar radiation that can cause degradation of the material. Adhesive tape shall not be permitted.
	R403.5.1 Heated water circulation and temperature maintenance systems (Mandatory). If heated water circulation systems are installed, they shall be in accordance with Section R403.5.1.1. Heat trace temperature maintenance systems shall be in accordance with Section R403.5.1.2. Automatic controls, temperature sensors and pumps shall be accessible. Manual controls shall be readily accessible.
	R403.5.1.1 Circulation systems. Heated water circulation systems shall be provided with a circulation pump. The system return pipe shall be a dedicated return pipe or a cold water supply pipe. Gravity and thermosiphon circulation systems shall be prohibited. Controls for circulating hot water system pumps shall start the pump based on the identification of a demand for hot water within the occupancy. The controls shall automatically turn off the pump when the water in the circulation loop is at the desired temperature and when there is no demand for hot water.
	R403.5.1.2 Heat trace systems. Electric heat trace systems shall comply with IEEE 515.1 or UL 515. Controls for such systems shall automatically adjust the energy input to the heat tracing to maintain the desired water temperature in the piping in accordance with the times when heated water is used in the occupancy.

R402.4.5 Recessed lighting. Recessed luminaires installed in the building thermal envelope shall be sealed to limit air leakage between conditioned and unconditioned spaces. All recessed luminaires shall be IC-rated and labeled as having an air leakage rate

MANDATORY REQUIREMENTS (Continued)

R403.5.5 Heat traps (Mandatory). Storage water heaters not equipped with integral heat traps and having vertical pipe risers shall have heat traps installed on both the inlets and outlets. External heat traps shall consist of either a commercially available heat trap or a downward and upward bend of at least 3 ½ inches (89 mm) in the hot water distribution line and cold water line located as close as possible to the storage tank.
R403.5.6 Water heater efficiencies (Mandatory). R403.5.6.1.1 Automatic controls. Service water-heating systems shall be equipped with automatic temperature controls capable of adjustment from the lowest to the highest acceptable temperature settings for the intended use. The minimum temperature setting range shall be from 100°F to 140°F (38°C to 60°C).
R403.5.6.1.2 Shut down. A separate switch or a clearly marked circuit breaker shall be provided to permit the power supplied to electric service systems to be turned off. A separate valve shall be provided to permit the energy supplied to the main burner(s) of combustion types of service water-heating systems to be turned off.
R403.5.6.2 Water-heating equipment. Water-heating equipment installed in residential units shall meet the minimum efficiencies of Table C404.2 in Chapter 4 of the Florida Building Code, Energy Conservation, Commercial Provisions, for the type of equipment installed. Equipment used to provide heating functions as part of a combination system shall satisfy all stated requirements for the appropriate water-heating category. Solar water heaters shall meet the criteria of Section R403.5.6.2.1.
R403.5.6.2.1 Solar water-heating systems. Solar systems for domestic hot water production are rated by the annual solar energy factor of the system. The solar energy factor of a system shall be determined from the Florida Solar Energy Center Directory of Certified Solar Systems. Solar collectors shall be tested in accordance with ISO Standard 9806 Test Methods for Solar Collectors, and SRCC Standard TM-1, Solar Domestic Hot Water System and Component Test Protocol. Collectors in installed solar water-heating systems should meet the following criteria: 1. Be installed with a tilt angle between 10 degrees and 40 degrees of the horizontal; and 2. Be installed at an orientation within 45 degrees of true south.
R403.6 Mechanical ventilation (Mandatory). The building shall be provided with ventilation that meets the requirements of the Florida Building Code, Residential, or Florida Building Code, Mechanical, as applicable, or with other approved means of ventilation including: Natural, Infiltration or Mechanical means. Outdoor air intakes and exhausts shall have automatic or gravity dampers that close when the ventilation system is not operating.
R403.6.1 Whole-house mechanical ventilation system fan efficacy. When installed to function as a whole-house mechanical ventilation system, fans shall meet the efficacy requirements of Table R403.6.1.
Exception: Where an air handler that is integral to tested and listed HVAC equipment is used to provide whole-house mechanical ventilation, the air handler shall be powered by an electronically commutated motor.
R403.6.2 Ventilation Air. Residential buildings designed to be operated at a positive indoor pressure or for mechanical ventilation shall meet the following criteria:
 The design air change per hour minimums for residential buildings in ASHRAE 62.2, Ventilation for Acceptable Indoor Air Quality, shall be the maximum rates allowed for residential applications.
No ventilation or air-conditioning system make-up air shall be provided to conditioned space from attics, crawlspaces, attached enclosed garages or outdoor spaces adjacent to swimming pools or spas.
3. If ventilation air is drawn from enclosed space(s), then the walls of the space(s) from which air is drawn shall be insulated to a minimum of R-11 and the ceiling shall be insulated to a minimum of R-19, space permitting, or R-10 otherwise.
R403.7.1 Equipment sizing (Mandatory). Heating and cooling equipment shall be sized in accordance with ACCA Manual S based on the equipment loads calculated in accordance with ACCA Manual J or other approved heating and cooling calculation methodologies, based on building loads for the directional orientation of the building. The manufacturer and model number of the outdoor and indoor units (if split system) shall be submitted along with the sensible and total cooling capacities at the design conditions described in Section R302.1. This Code does not allow designer safety factors, provisions for future expansion or other factors that affect equipment sizing. System sizing calculations shall not include loads created by local intermittent mechanical ventilation such as standard kitchen and bathroom exhaust systems. New or replacement heating and cooling equipment shall have an efficiency rating equal to or greater than the minimum required by federal law for the geographic location where the equipment is installed.

MANDATORY REQUIREMENTS (Continued)

TABLE R403.6.1 WHOLE-HOUSE MECHANICAL VENTILATION SYSTEM FAN EFFICACY

FAN LOCATION	AIRFLOW RATE MINIMUM (CFM)	MINIMUM EFFICACY ^a (CFM/WATT)	AIRFLOW RATE MAXIMUM (CFM)
HRV or ERV	Any	1.2 cfm/watt	Any
Rangehoods	Any	2.8 cfm/watt	Any
In-line fan	Any	2.8 cfm/watt	Any
Bathroom, utility room	10	1.4 cfm/watt	<90
Bathroom, utility room	90	2.8 cfm/watt	Any

For SI: 1 cfm = 28.3 L/min.

R403.7.1.1 Cooling equipment capacity. Cooling only equipment shall be selected so that its total capacity is not less than the calculated total load but not more than 1.15 times greater than the total load calculated according to the procedure selected in Section R403.7, or the closest available size provided by the manufacturer's product lines. The corresponding latent capacity of the equipment shall not be less than the calculated latent load.

The published value for AHRI total capacity is a nominal, rating-test value and shall not be used for equipment sizing. Manufacturer's expanded performance data shall be used to select cooling-only equipment. This selection shall be based on the outdoor design dry-bulb temperature for the load calculation (or entering water temperature for water-source equipment), the blower CFM provided by the expanded performance data, the design value for entering wet-bulb temperature and the design value for entering dry-bulb temperature.

Design values for entering wet-bulb and dry-bulb temperatures shall be for the indoor dry bulb and relative humidity used for the load calculation and shall be adjusted for return side gains if the return duct(s) is installed in an unconditioned space.

Exceptions:

- 1. Attached single- and multiple-family residential equipment sizing may be selected so that its cooling capacity is less than the calculated total sensible load but not less than 80 percent of that load.
- 2. When signed and sealed by a Florida-registered engineer, in attached single- and multiple-family units, the capacity of equipment may be sized in accordance with good design practice.

R403.7.1.2 Heating equipment capacity.

R403.7.1.2.1 Heat pumps. Heat pump sizing shall be based on the cooling requirements as calculated according to Section R403.7.1.1, and the heat pump total cooling capacity shall not be more than 1.15 times greater than the design cooling load even if the design heating load is 1.15 times greater than the design cooling load.
R403.7.1.2.2 Electric resistance furnaces. Electric resistance furnaces shall be sized within 4 kW of the design requirements calculated according to the procedure selected in Section R403.7.1.
R403.7.1.2.3 Fossil fuel heating equipment. The capacity of fossil fuel heating equipment with natural draft atmospheric burners shall not be less than the design load calculated in accordance with Section R403.7.1.
R403.7.1.3 Extra capacity required for special occasions. Residences requiring excess cooling or heating equipment capacity on an intermittent basis, such as anticipated additional loads caused by major entertainment events, shall have equipment sized or controlled to prevent continuous space cooling or heating within that space by one or more of the following options: 1. A separate cooling or heating system is utilized to provide cooling or heating to the major entertainment areas. 2. A variable capacity system sized for optimum performance during base load periods is utilized.
R403.8 Systems serving multiple dwelling units (Mandatory). Systems serving multiple dwelling units shall comply with Sections C403 and C404 of the Florida Building Code, Energy Conservation—Commercial Provisions in lieu of Section R403.
R403.9 Snow melt and ice system controls (Mandatory). Snow- and ice-melting systems, supplied through energy service to the building, shall include automatic controls capable of shutting off the system when the pavement temperature is above 50°F (10°C), and no precipitation is falling and an automatic or manual control that will allow shutoff when the outdoor temperature is above 40°F (4.8°C).
403.10 Pools and permanent spa energy consumption (Mandatory). The energy consumption of pools and permanent spas shall be in accordance with Sections R403.10.1 through R403.10.5.
R403.10.1 Heaters. The electric power to heaters shall be controlled by a readily accessible on-off switch that is an integral part of the heater mounted on the exterior of the heater, or external to and within 3 feet (914 mm) of the heater. Operation of such switch shall not change the setting of the heater thermostat. Such switches shall be in addition to a circuit breaker for the power to the heater.

Gas-fired heaters shall not be equipped with continuously burning ignition pilots.

a. When tested in accordance with HVI Standard 916

MANDATORY REQUIREMENTS (Continued) **R403.10.2 Time switches.** Time switches or other control methods that can automatically turn off and on according to a preset schedule shall be installed for heaters and pump motors. Heaters and pump motors that have built-in time switches shall be in compliance with this section. **Exceptions:** 1. Where public health standards require 24-hour pump operation. 2. Pumps that operate solar- and waste-heat-recovery pool heating systems 3. Where pumps are powered exclusively from on-site renewable generation. R403.10.3 Covers. Outdoor heated swimming pools and outdoor permanent spas shall be equipped with a vapor-retardant cover on or at the water surface or a liquid cover or other means proven to reduce heat loss. **Exception:**Where more than 70 percent of the energy for heating, computed over an operation season, is from site-recovered energy, such as from a heat pump or solar energy source, covers or other vapor-retardant means shall not be required R403.10.4 Gas- and oil-fired pool and spa heaters. All gas- and oil-fired pool and spa heaters shall have a minimum thermal efficiency of 82 percent for heaters manufactured on or after April 16, 2013, when tested in accordance with ANSI Z 21.56. Pool heaters fired by natural or LP gas shall not have continuously burning pilot lights. R403.10.5 Heat pump pool heaters. Heat pump pool heaters shall have a minimum COP of 4.0 when tested in accordance with AHRI 1160, Table 2, Standard Rating Conditions-Low Air Temperature. A test report from an independent laboratory is required to verify procedure compliance. Geothermal swimming pool heat pumps are not required to meet this standard. R403.11 Portable spas (Mandatory). The energy consumption of electric-powered portable spas shall be controlled by the requirements of APSP-14 **R403.13 Dehumidifiers (Mandatory).** If installed, a dehumidifier shall conform to the following requirements: 1. The minimum rated efficiency of the dehumidifier shall be greater than 1.7 liters/ kWh if the total dehumidifier capacity for the house is less than 75 pints/day and greater than 2.38 liters/kWh if the total dehumidifier capacity for the house is greater than or equal to 75 pints/day. 2. The dehumidifier shall be controlled by a sensor that is installed in a location where it is exposed to mixed house air. 3. Any dehumidifier unit located in unconditioned space that treats air from conditioned space shall be insulated to a minimum of R-2. 4. Condensate disposal shall be in accordance with Section M1411.3.1 of the Florida Building Code, Residential.

- R403.13.1 Ducted dehumidifiers. Ducted dehumidifiers shall, in addition to conforming to the requirements of Section R403.13, conform to the following requirements:
 - If a ducted dehumidifier is configured with return and supply ducts both connected into the supply side of the cooling system, a backdraft damper shall be installed in the supply air duct between the dehumidifier inlet and outlet duct.
 - 2. If a ducted dehumidifier is configured with only its supply duct connected into the supply side of the central heating and cooling system, a backdraft damper shall be installed in the dehumidifier supply duct between the dehumidifier and central supply duct.
 - 3. A ducted dehumidifier shall not be ducted to or from a central ducted cooling system on the return duct side upstream from the central cooling evaporator coil.
 - 4. Ductwork associated with a dehumidifier located in unconditioned space shall be insulated to a minimum of R-6.

SECTION R404 ELECTRICAL POWER AND LIGHTING SYSTEMS

R404.1 Lighting equipment (Mandatory). Not less than 90 percent of the lamps in permanently installed luminaires shall have an efficacy of at least 45 lumens-per-watt or shall utilize lamps with an efficacy of not less than 65 lumens-per-watt.

R404.1.1 Lighting equipment (Mandatory). uel gas lighting systems shall not have continuously burning pilot lights.

2020 - AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA TABLE 402.4.1.1

AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA®

19TH ST SW Project Name: Builder Name:

Permit Office: COLLIER COUNTY Street: 19TH ST SW

City, State, Zip: NAPLES, FL, 34117 Permit Number:

PEREZ REINIER & MASSIEL SANABRIA Jurisdiction: 211200 Owner:

Design Location:	FL, NAPLES_MUNICIPAL	County:	Collier(Florida Climate Zone 1)	뿡
COMPONENT	AIR BARRIER CRITERIA		INSULATION INSTALLATION CRITERIA	
General requirements	A continuous air barrier shall be installed in the building en The exterior thermal envelope contains a continuous air ba Breaks or joints in the air barrier shall be sealed.		Air-permeable insulation shall not be used as a sealing material.	
Ceiling/attic	The air barrier in any dropped ceiling/soffit shall be aligned the insulation and any gaps in the air barrier shall be sealed Access openings, drop down stairs or knee wall doors to unconditioned attic spaces shall be sealed.		The insulation in any dropped ceiling/soffit shall be aligned with the air barrier.	
Walls	The junction of the foundation and sill plate shall be sealed. The junction of the top plate and the top of exterior walls s sealed. Knee walls shall be sealed.		Cavities within corners and headers of frame walls shall be insulated by completely filling the cavity with a material having a thermal resistance of R-3 per inch minimum Exterior thermal envelope insulation for framed walls shall be installed in substantial contact and continuous alignment with the air barrier.	
Windows, skylights and doors	The space between window/door jambs and framing, and skylights and framing shall be sealed.			
Rim joists	Rim joists shall include the air barrier.		Rim joists shall be insulated.	
Floors (including above-garage andcantilevered floors)	The air barrier shall be installed at any exposed edge of insulation.		Floor framing cavity insulation shall be installed to maintain permanent contact with the underside of subfloor decking, or floor framing cavity insulation shall be permitted to be in contact with the top side of sheathing, or continuous insulation installed on the underside of floor framing and extends from the bottom to the top of all perimeter floor framing members.	
Crawl space walls	Exposed earth in unvented crawl spaces shall be covered with a Class I vapor retarder with overlapping joints taped.		Where provided instead of floor insulation, insulation shall be permanently attached to the crawlspace walls.	
Shafts,penetrations	Duct shafts, utility penetrations, and flue shafts opening to exterior or unconditioned space shall be sealed.			
Narrowcavities			Batts in narrow cavities shall be cut to fit, or narrow cavities shall be filled by insulation that on installation readily conforms to the available cavity spaces.	
Garageseparation	Air sealing shall be provided between the garage and conditioned spaces.			
Recessedlighting	Recessed light fixtures installed in the building thermal envelope shall be sealed to the finished surface.		Recessed light fixtures installed in the building thermal envelope shall be air tight and IC rated.	
Plumbing and wiring			Batt insulation shall be cut neatly to fit around wiring and plumbing in exterior walls, or insulation that on installation readily conforms to available space shall extend behind piping and wiring.	
Shower/tub on exterior wall	The air barrier installed at exterior walls adjacent to showe and tubs shall separate them from the showers and tubs.	ers	Exterior walls adjacent to showers and tubs shall be insulated.	
Electrical/phonebox on exterior walls	The air barrier shall be installed behind electrical or communication boxes or air-sealed boxes shall be installed	d.		
HVAC register boots	HVAC supply and return register boots that penetrate builthermal envelope shall be sealed to the sub-floor, wall covor ceiling penetrated by the boot.			
Concealed sprinklers	When required to be sealed, concealed fire sprinklers sha be sealed in a manner that is recommended by the manuf- Caulking or other adhesive sealants shall not be used to fi voids between fire sprinkler cover plates and walls or ceilin	acturer. Il voids		

a. In addition, inspection of log walls shall be in accordance with the provisions of ICC-400.

ECK

Envelope Leakage Test Report (Blower Door Test) Residential Prescriptive, Performance or ERI Method Compliance 2020 Florida Building Code, Energy Conservation, 7th Edition

Jurisdiction: 211200	Permit #:			
Job Information				
Builder: Community:	Lot: NA			
Address: 19TH ST SW				
City: NAPLES State	e: FL Zip: 34117			
Air Leakage Test Results Passing results must meet	either the Performance, Prescriptive, or ERI Method			
PRESCRIPTIVE METHOD-The building or dwelling unit shall be tested and verified as having an air leakage rate of not exceeding 7 air changes per hour at a pressure of 0.2 inch w.g. (50 Pascals) in Climate Zones 1 and 2.				
PERFORMANCE or ERI METHOD-The building or dwelling unit shat the selected ACH(50) value, as shown on Form R405-2020 (Performance) of ACH(50) specified on Form R405-2020-Energy Calc	or R406-2020 (ERI), section labeled as infiltration, sub-section ACH50.			
x 60 ÷ 15181 = ACH(50) PASS When ACH(50) is less than 3, Mechanical Ventilation must be verified by building department.	Method for calculating building volume: ○ Retrieved from architectural plans ○ Code software calculated installation ○ Field measured and calculated			
R402.4.1.2 Testing. Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 Pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), Florida Statues.or individuals licensed as set forth in Section 489.105(3)(f), (g), or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the code official. Testing shall be performed at any time after creation of all penetrations of the building thermal envelope.				
During testing: 1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration controlmeasures. 2. Dampers including exhaust, intake, makeup air, back draft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures. 3. Interior doors, if installed at the time of the test, shall be open. 4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed. 5. Heating and cooling systems, if installed at the time of the test, shall be turned off. 6. Supply and return registers, if installed at the time of the test, shall be fully open.				
Testing Company				
Company Name: Phone: Phone: I hereby verify that the above Air Leakage results are in accordance with the 2020 7th Edition Florida Building Code Energy Conservation requirements according to the compliance method selected above.				
Signature of Tester: Date of Test: Printed Name of Tester:				
			License/Certification #:	Issuing Authority:

Duct Leakage Test Report

Residential Prescriptive, Performance or ERI Method Compliance 2020 Florida Building Code, Energy Conservation, 7th Edition

Jurisdiction:	211200		Permit #:	
Job Information				
Builder:		Community:		Lot: NA
Address: 19TH ST	SW			
City: NAPLES		State	e: FL	Zip: 34117
Duct Leakage Te	est Results			
System 1	cfm25	○ Prescriptiv	ve Method cfm25 (Total)
System 2	cfm25	To qualify as	"substantially leak free	" Qn Total must be less than or stalled. If air handler unit is not
System 3	cfm25	installed, Qn	Total must be less than	n or equal to 0.03. This testing
Sum of others	cfm25	method meets the requirements in accordance with Section R403.3.3. Is the air handler unit installed during testing? YES (= 0.4 or NO (= 0.4 or NO)) Performance/ERI Method cfm25 (Out or Total)		
Total of all	cfm25			
	FAIL verified by testing in ac	proposed due Leakage Typ R405-2020 (Ene Default Lea	et leakage Qn specified e selected on Form ergyCalc) or R406-2020 akage /RESNET/ICC380 by eith	on Form R405-2020 or R406-2020. Qn specified on Form R405-2020 (EnergyCalc) or R406-2020 0.00 Deer individuals as defined in Section (f), (g) or (i), Florida Statutes.
Testing Company				
Company Name: Phone: Phone: I hereby verify that the above duct leakage testing results are in accordance with the Florida Building Code requirements with the selected compliance path as stated above, either the Prescriptive Method or Performance Method.				
Signature of Tester:	:		Date of Tes	t:
Printed Name of Tester:				
License/Certificatio	n#:		Issuing Auth	nority:
